

中防北水路 処理水圧送施設更新工事のお知らせ

工期: 令和7年12月18日～令和10年2月29日のうち令和8年7月8日～令和8年10月26日

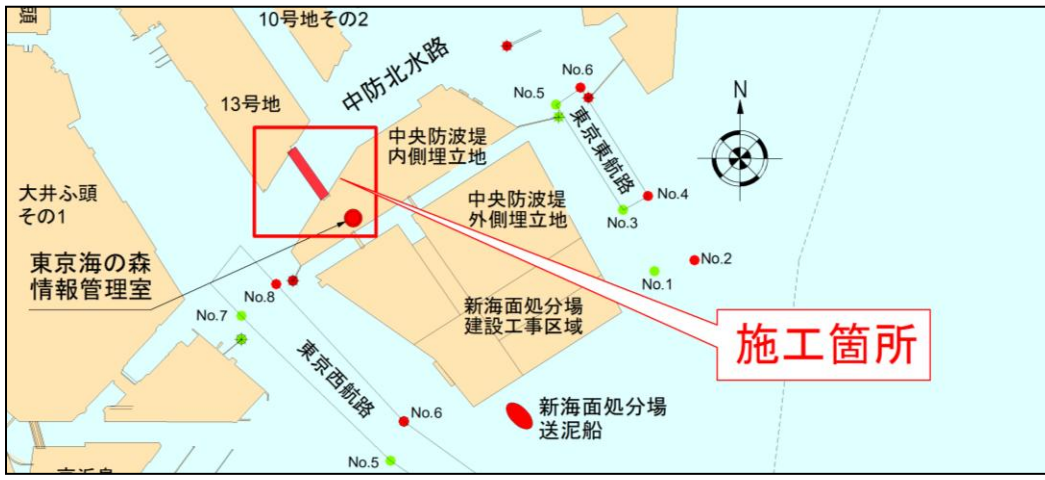


図-1 案内図

<p>①床掘工(試掘)・人力掘削 7月 8日～7月25日(予定) 7月30日～8月17日(予定)</p>	<p>②床掘工(ポンド掘削) 7月 26日～7月 29日(予定)</p>
<p>③架台撤去工 北側 8月 18日～8月 19日(予定)</p>	<p>④架台撤去工 南側 8月 20日～8月 21日(予定)</p>
<p>⑤床掘工 北側・人力掘削※ 8月 22日～8月 31日(予定) 9月 20日～10月 26日(予定)</p>	<p>⑥床掘工 ジェット併用ポンプ掘削・人力掘削※ 9月 1日～9月 14日(予定)</p>
<p>⑦人力掘削</p> <p>警戒船を2隻、中防北水路外に配備し作業を実施します。</p>	<p>全長100mを超える船舶の通航がある場合等、人力掘削のみの作業となることがあります。</p>

※上記、作業①、⑤、⑥の際、航路内作業(作業船の使用)を中止した場合は、人力掘削のみの作業となります。安全対策及び可航幅は作業⑦と同様になります。
※日程は変更する場合がありますので、右下のQRコードからホームページでご確認ください。
※事前にメールアドレスをご連絡いただければ、変更の都度、メールにてご連絡いたします。

図-2 各工程の通航帯

<p>北側施工時</p> <p>灯浮標設置・撤去時の通航路</p>	<p>南側施工時</p> <p>灯浮標設置・撤去時の通航路</p>
<p>●灯浮標設置・撤去時の通航路は床掘作業時の通航路と異なります。</p>	
<p>灯浮標設置後、床掘作業時の通航路</p> <p>全長50m以下の船舶 相互通航可能</p>	
<p>●相互通航可能ですので対向船舶に気を付けて通航してください。</p>	
<p>全長50m～100m以下の船舶 西航船は工作業区域手前で待機、東航船通過後、西航船が通航</p>	
<p>●東航船が50m～100m以下の船舶の場合、東航船通過まで西航船は工作業区域東側で一待機をお願いします。</p>	
<p>全長100m超の船舶 工所用船舶は、一般船舶の操船の支障とならない位置へ退避</p>	
<p>●安全な工事の中断を図るため100メートルを超える船舶が工事海域を航行したい場合は3時間前までに東京海の森航行安全情報管理室に連絡してください。なお、工事海域を航行する3時間前までの連絡がない場合は安全な工事の中断ができないため、お待ち頂くか迂回をお願いします。</p>	

図-3 工事箇所付近の通航方法

Notice of Central Breakwater North Waterway Treated Water Pressurized Transfer Facility Renovation Construction

Construction period: December 18, 2025 to February 29, 2028 including the period of July 8, 2026 to October 26, 2026

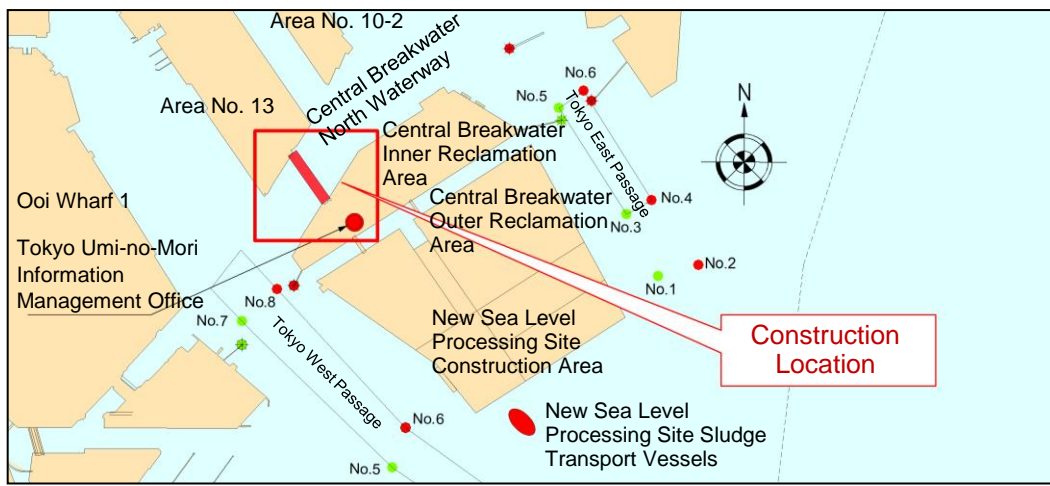


Figure-1 Guide Diagram

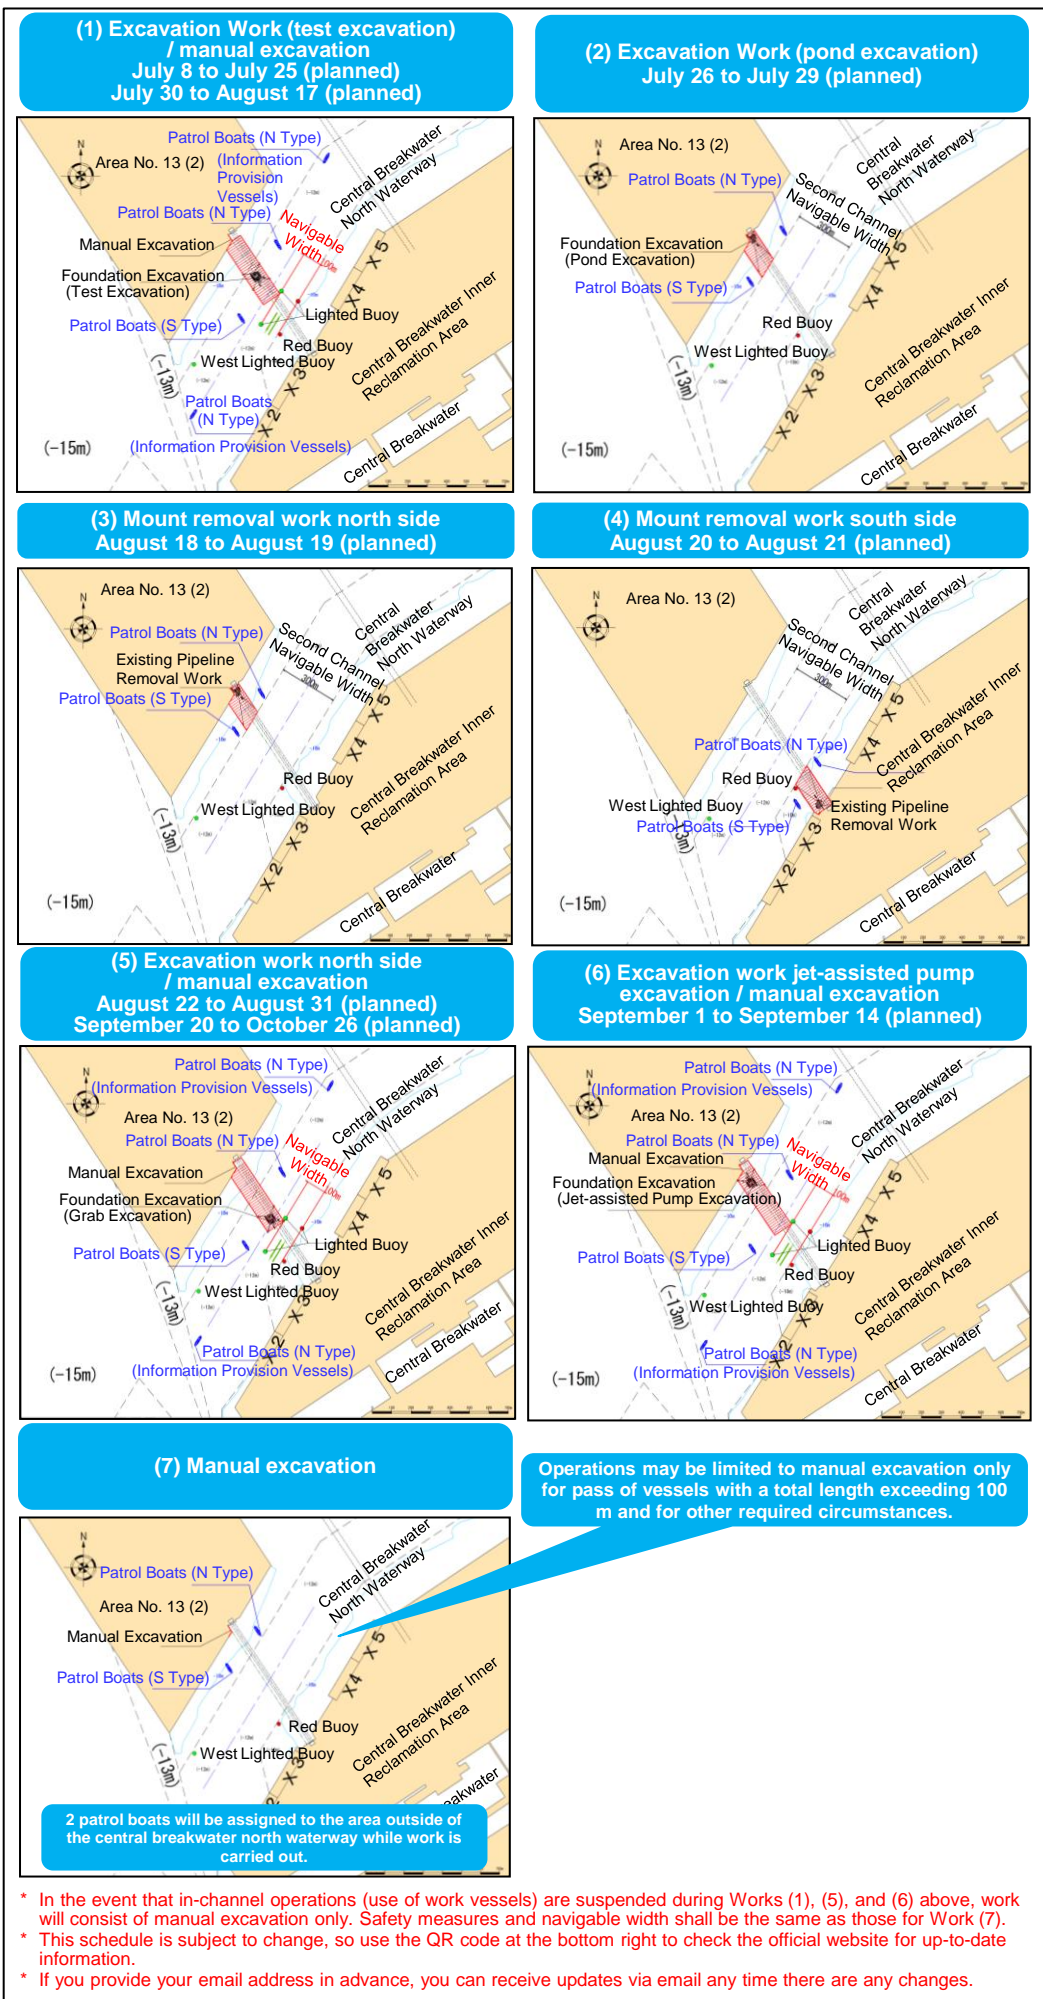


Figure-2 Navigable Lanes for Each Construction Phase

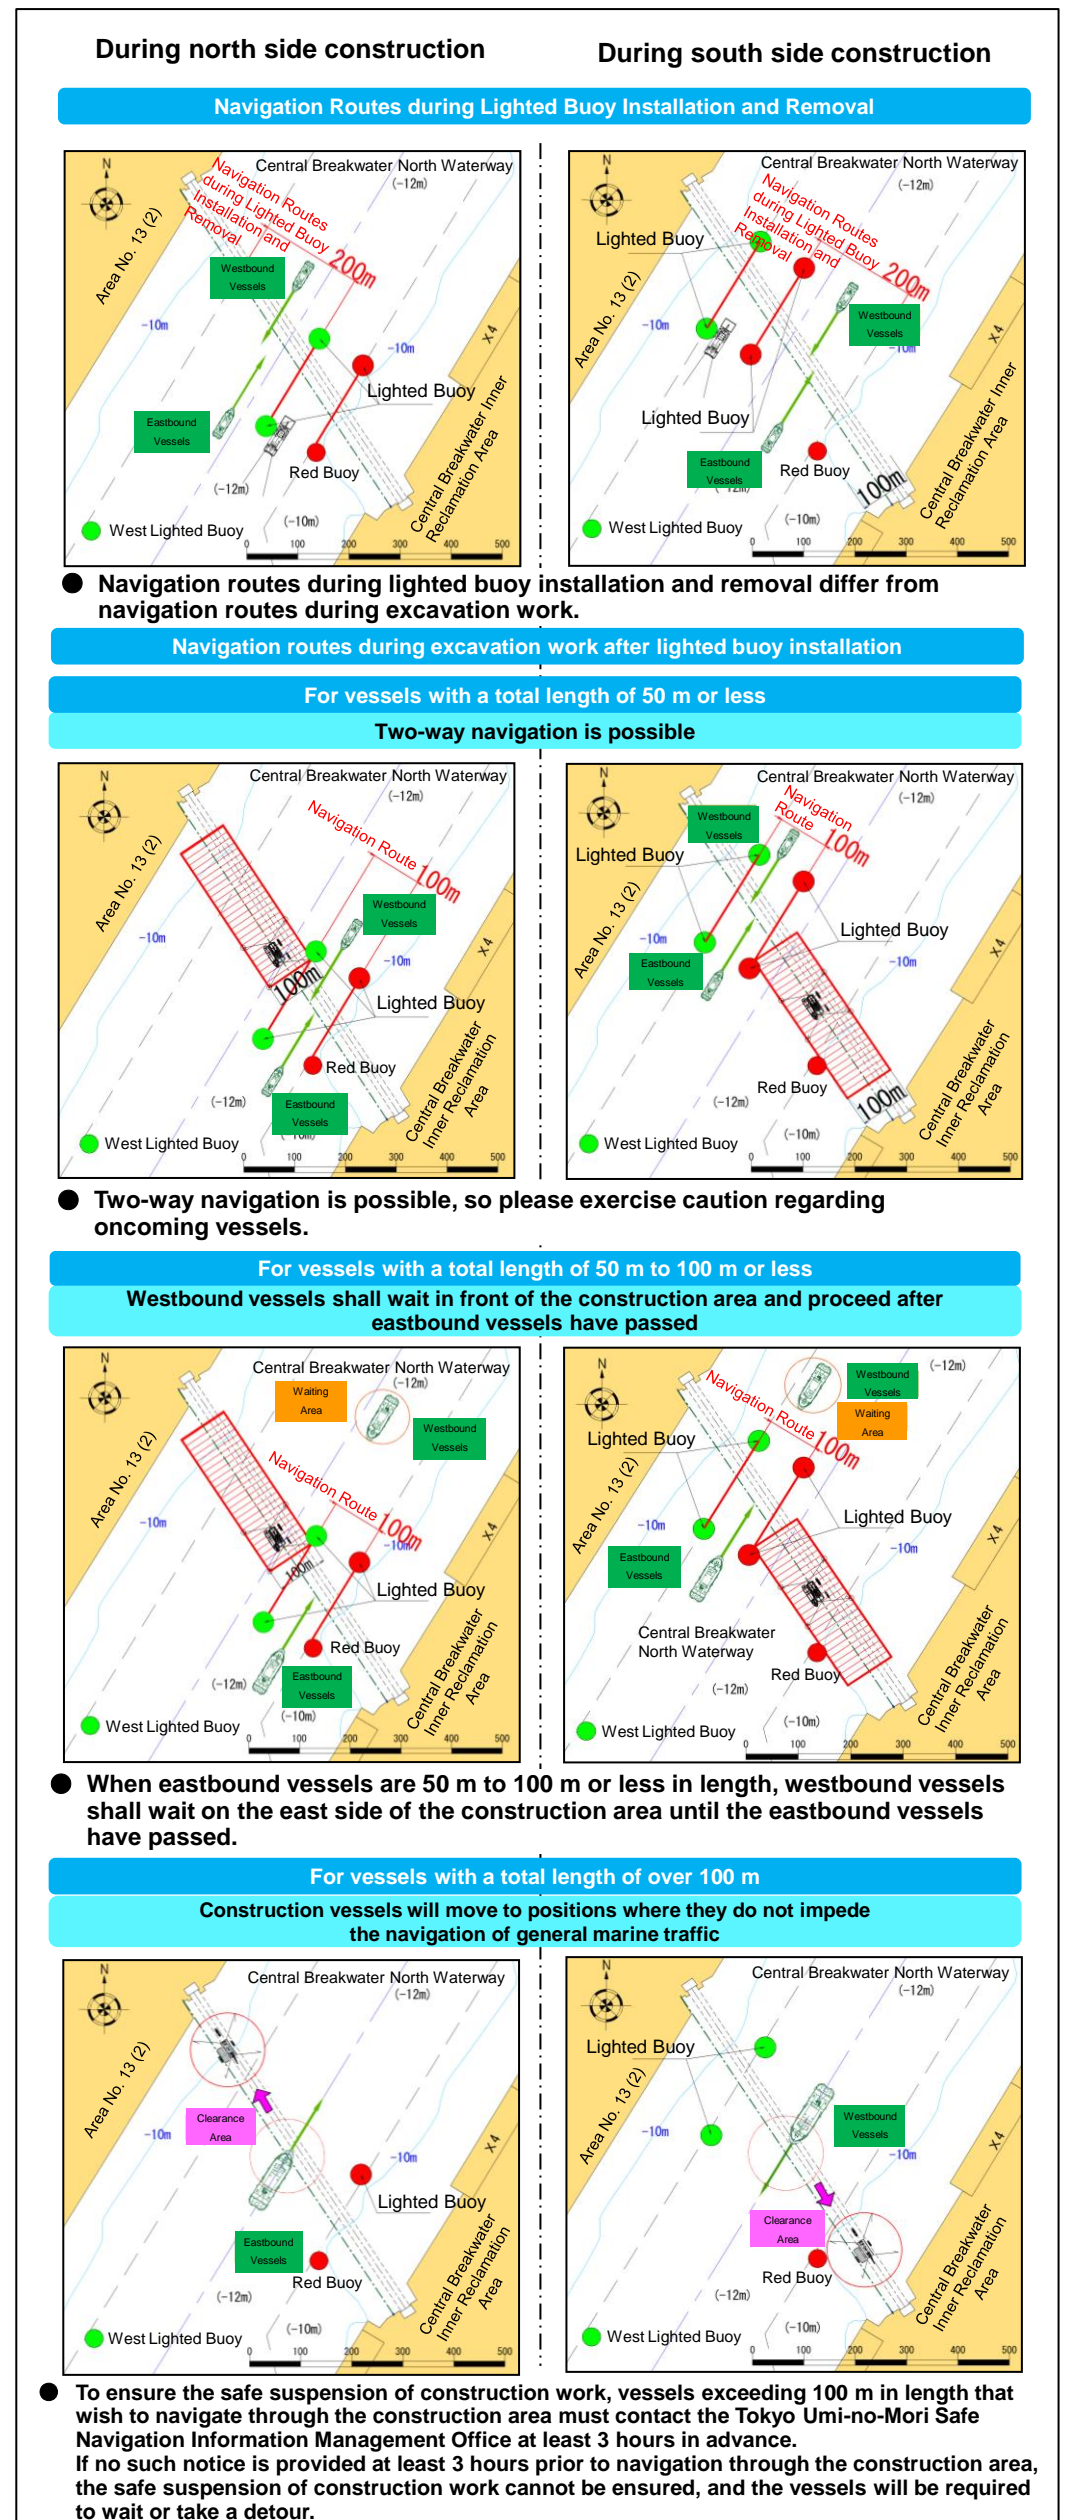


Figure-3 Navigation Methods Near Construction Locations

Inquiries

Contracting Authority
Tokyo Metropolitan Government Bureau of
Environment Waste Landfill Site Office
Tel.: 03-5531-3713

Contractor
TOA Corporation Tokyo Branch Port of Tokyo Construction Office
Aomi Pressure Pipeline Renovation Worksite
Tokyo Umi-no-Mori Safe Navigation Information Management Office
Tel.: 03-5962-4281 e-mail: uminomori2026@gmail.com



Find the latest information here

* In the event that in-channel operations (use of work vessels) are suspended during Works (1), (5), and (6) above, work will consist of manual excavation only. Safety measures and navigable width shall be the same as those for Work (7).
* This schedule is subject to change, so use the QR code at the bottom right to check the official website for up-to-date information.
* If you provide your email address in advance, you can receive updates via email any time there are any changes.
